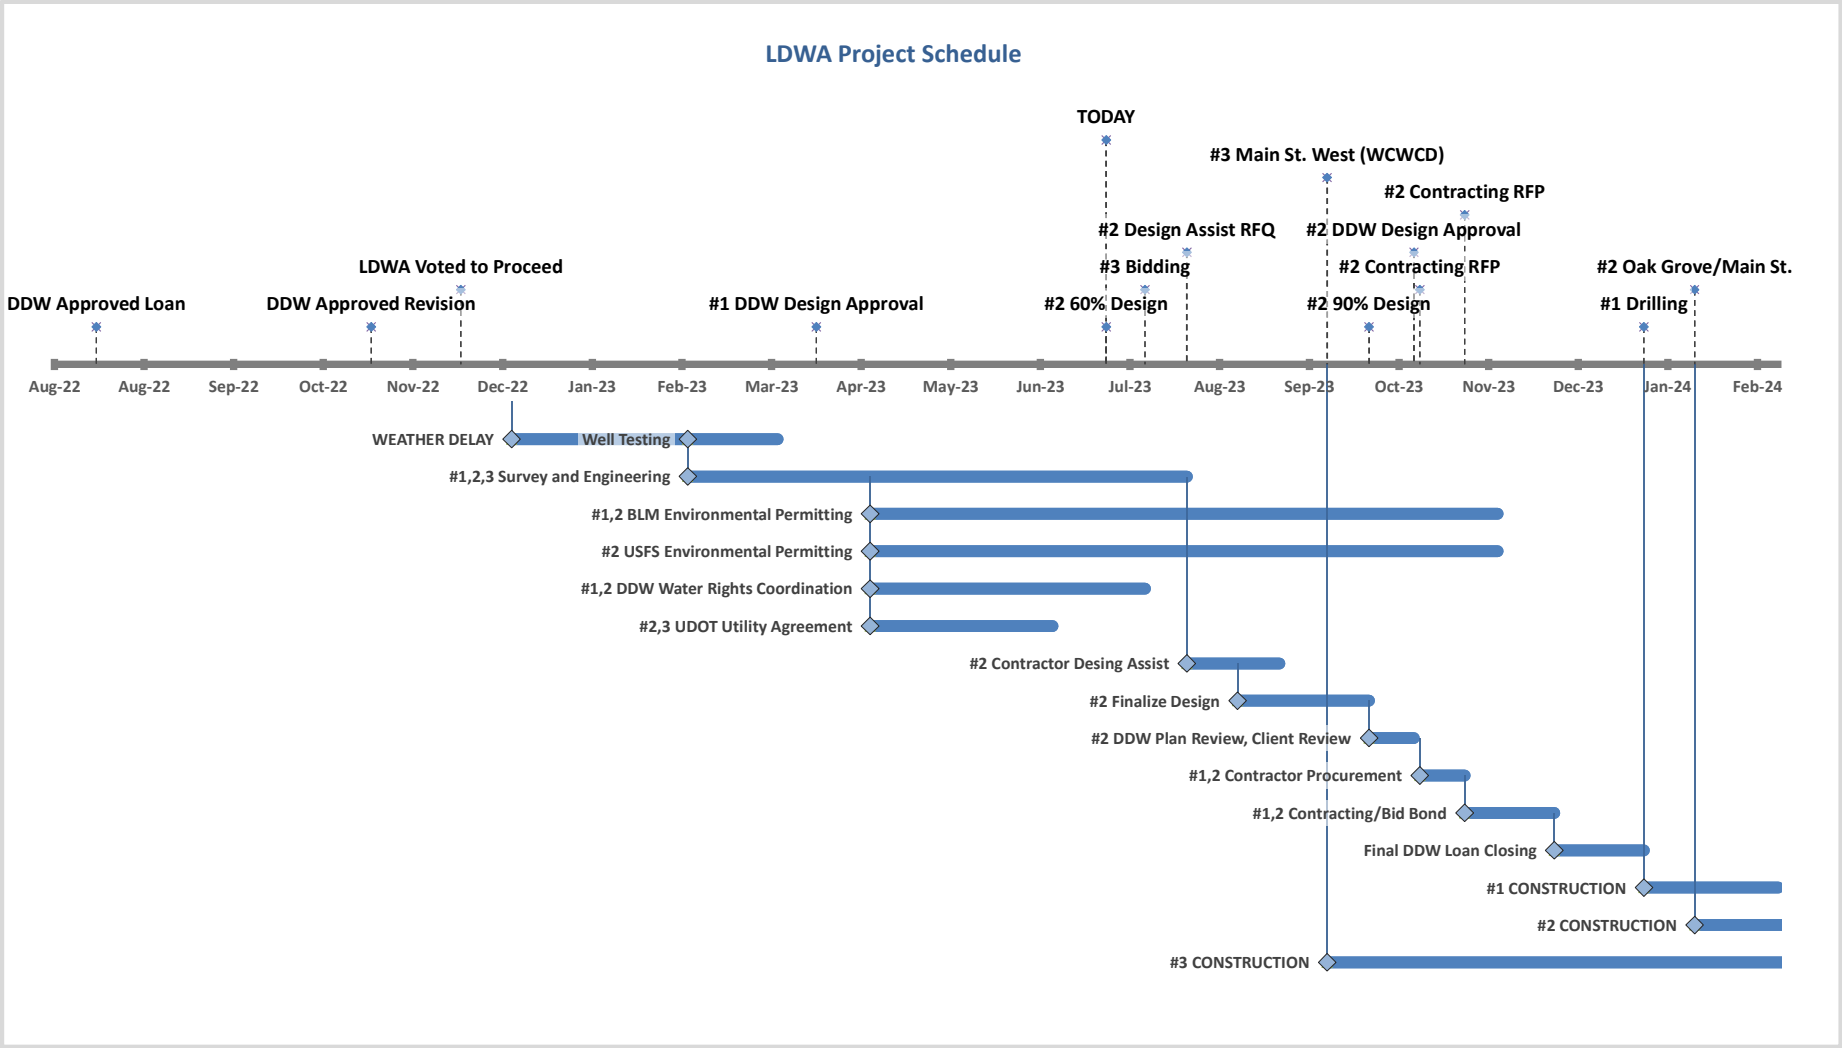
LDWA Project Schedule
TODAY
#3 Main St. West (WCWCD)
#2 Contracting RFP
#2 Design Assist RFQ
#2 DDW Design Approval
LDWA Voted to Proceed
#3 Bidding
#2 Contracting RFP
#2 Oak Grove/Main St.
DDW Approved Loan
DDW Approved Revision
#1 DDW Design Approval
#2 60% Design
#2 90% Design
#1 Drilling
Aug-22
Aug-22
Sep-22
Oct-22
Nov-22
Dec-22
Jan-23
Feb-23
Mar-23
Apr-23
May-23
Jun-23
Jul-23
Aug-23
Sep-23
Oct-23
Nov-23
Dec-23
Jan-24
Feb-24
WEATHER DELAY
Well Testing
#1,2,3 Survey and Engineering
#1,2 BLM Environmental Permitting
#2 USFS Environmental Permitting
#1,2 DDW Water Rights Coordination
#2,3 UDOT Utility Agreement
#2 Contractor Desing Assist
#2 Finalize Design
#2 DDW Plan Review, Client Review
#1,2 Contractor Procurement
#1,2 Contracting/Bid Bond
Final DDW Loan Closing
#1 CONSTRUCTION
#2 CONSTRUCTION
#3 CONSTRUCTION
